


Pair 5 is the approved priority initiative for responsible enterprise AI value.

Decision fact	Position
Selected initiative	Pair 5 – Integrated AI Banking Implementation Ecosystem
Selection result	92/100; 12 points ahead of the next-best option
Investment case	\$11.5M CAPEX; \$3.2M annual OPEX; \$27.5M five-year TCO; +\$9.1M five-year NPV
Delivery model	24-month, stage-gated programme with Agile MVP delivery inside Waterfall governance
Sponsor	Sheikh Moeen Akhtar


Pole Trust Bank is not pursuing isolated AI experiments. It is establishing a controlled enterprise foundation that enables four high-value, human-accountable use cases.

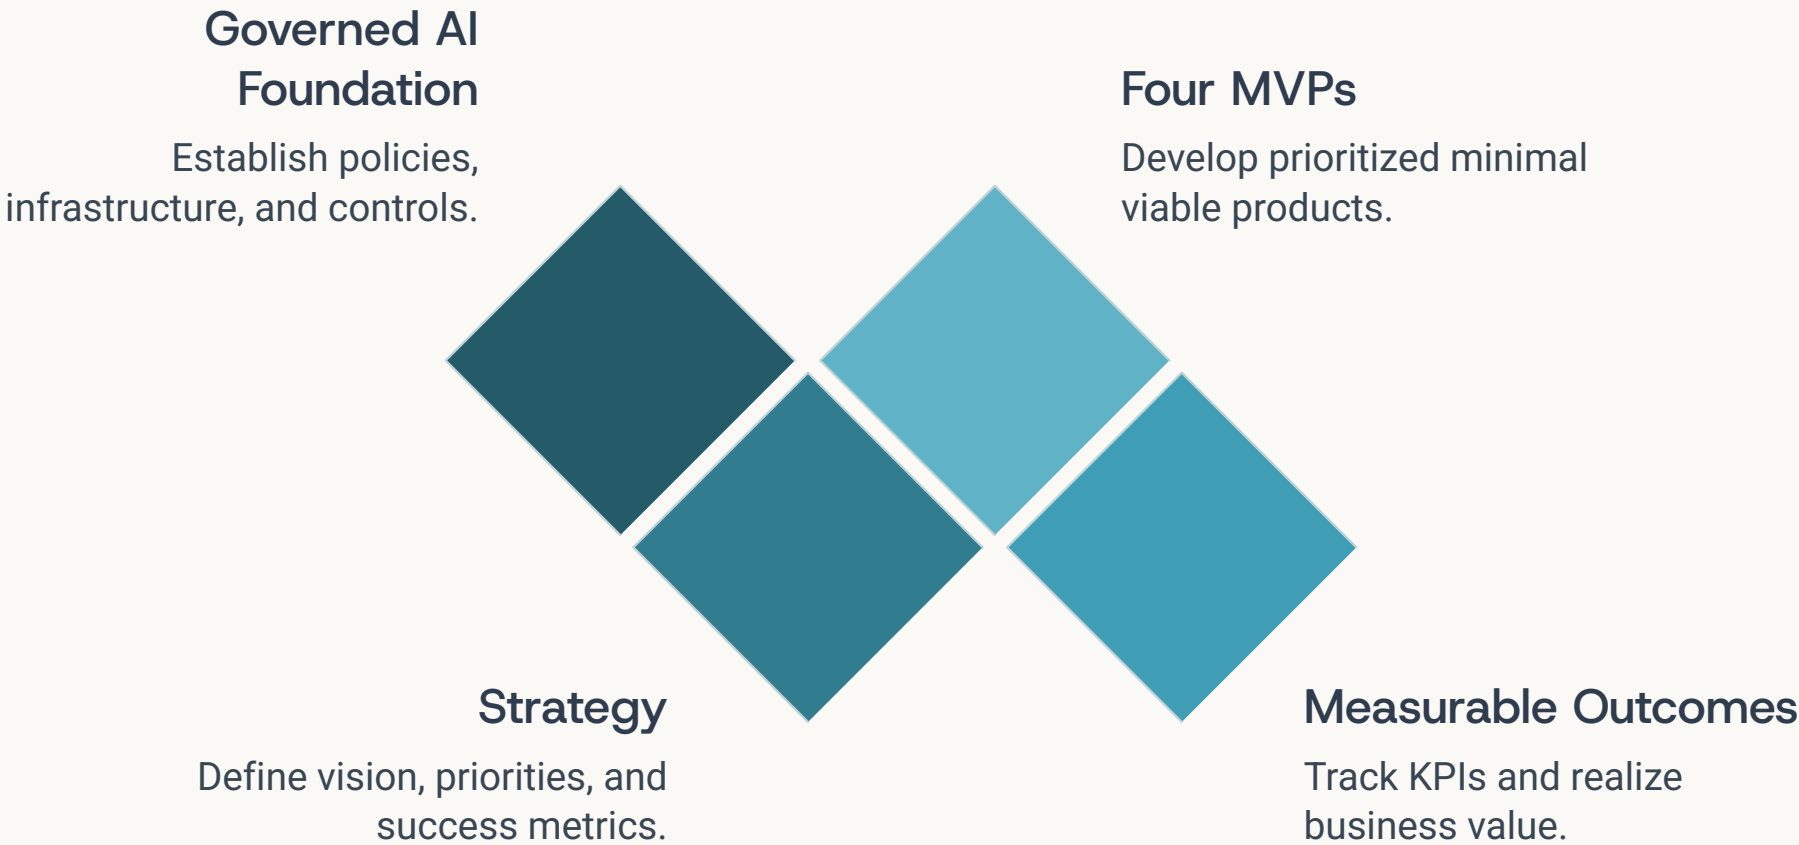

The complete planning pack is approved; its documents operate as one management system.

Document	Purpose	Integration with the other documents	Status
Document 1 – Selection, BC/FS	Establishes why Pair 5 is the priority	Provides value case, outcomes, risks and boundaries for the Charter	Approved
Document 2 – Project Charter	Establishes mandate, authority, milestones and planning envelope	Sets the governance frame for stakeholders and scope	Approved
Document 3 – Stakeholder Register	Establishes owners, engagement and evidence contributors	Supplies roles and acceptance/accountability routes for delivery	Approved
Document 4 – Scope Management Plan/WBS	Establishes deliverables, work packages, acceptance and change control	Converts Charter scope into controlled execution-ready planning	Approved – WBS correction incorporated

 **Approval record:** On 2 August 2026, the Sponsor described the overall document as excellent, requested only a WBS correction, and stated that no resubmission was required. The corrected WBS was incorporated on 3 August 2026.

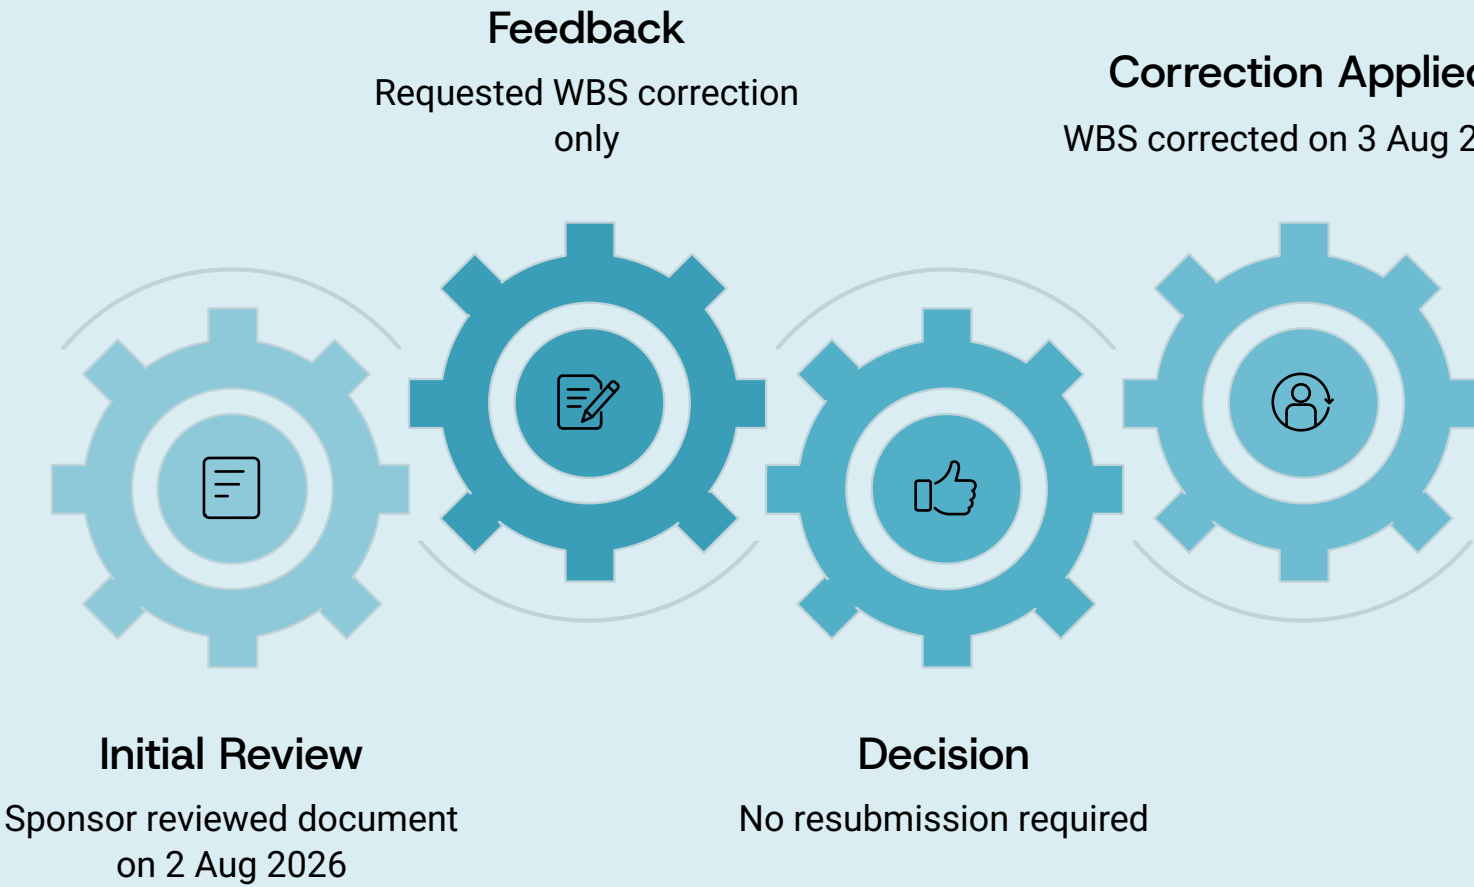


Why Pair 5 won: comparative value and trade-offs

Rank	Initiative	Score	Five-year NPV	Why it matters	Material constraint
1	Integrated ecosystem	92	+\$9.1M	Enterprise reach across service, productivity, lending and fraud	Requires disciplined governance, integration and benefit tracking
2	Customer digital assistant	80	+\$1.8M	Fast customer value and call-cost opportunity	Narrower strategic scope
=3	Lending support	73	+\$3.1M	Strong operational value	Explainability, fairness and human authority are critical
=3	Fraud enhancement	73	+\$4.3M	Strong risk-reduction potential	No automated adverse customer action
5	Internal copilot	72	-\$0.3M	Highly feasible, fast internal use case	Weak standalone economics

Decision criteria: strategic alignment 20%; business impact 20%; technical feasibility 15%; operational feasibility 15%; economic feasibility 15%; risk/compliance 10%; scalability/time to value 5%.

Insight: Pair 5 wins because it combines the strongest investment case with a reusable control and technology foundation, rather than optimizing a single narrow use case.

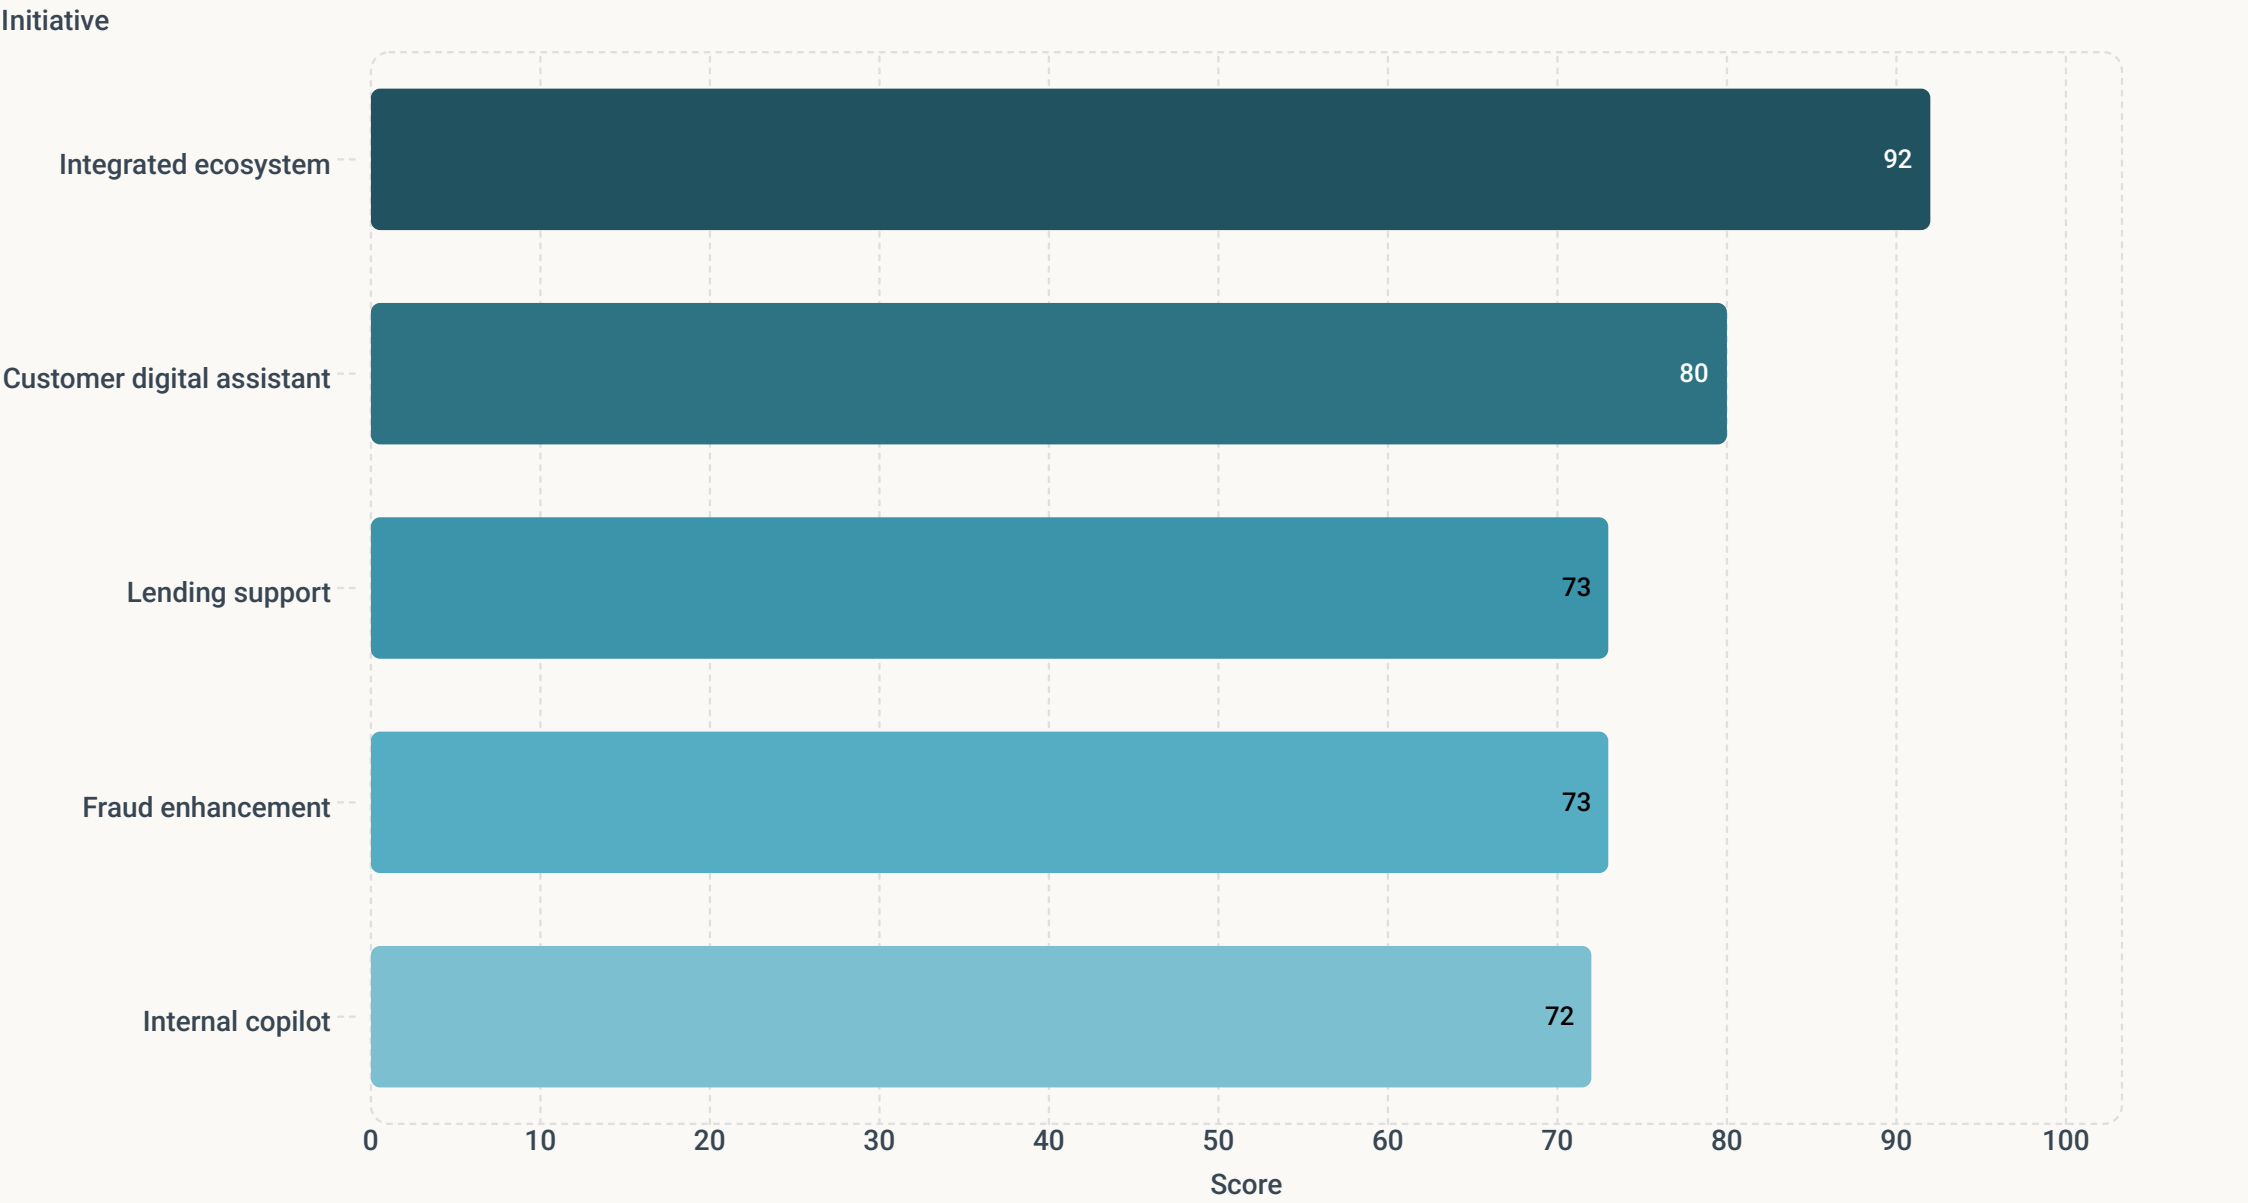


The programme delivers value through four controlled MVPs that share governance, data and integration capabilities.

MVP	Business outcome	Non-negotiable boundary
Internal productivity copilot	Reduce report-preparation time by 30%	Approved-source retrieval, access control and human verification
Customer digital assistant	Reduce repetitive customer inquiries by 35%	Privacy controls, approved knowledge and reliable human handoff
Lending support	Reduce documentation rework by 35%	Document/risk-summary assistance only; humans retain credit authority
Fraud investigator assist	Reduce false positives by 25% in pilot scope	Alert prioritization only; no automatic account action

Shared foundation: responsible AI; architecture and integration; data quality/lineage; identity/security/privacy; model risk; auditability; monitoring; incident management.

Explicit exclusions: autonomous credit/pricing decisions, unsupervised financial advice, automatic account blocking/freezing, replacement of core systems, ungated scale, unapproved personal-data reuse and vendor commitment before approval.

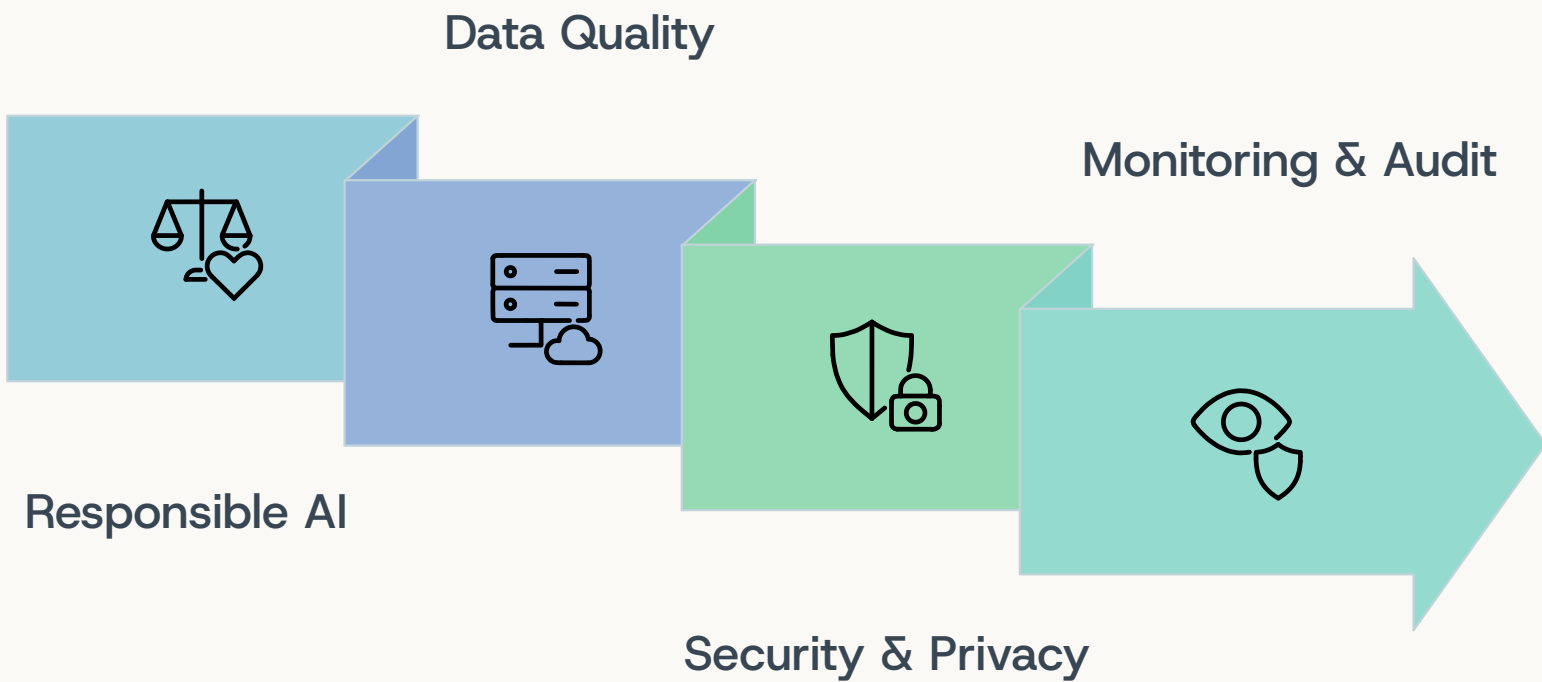


Charter: delivery route, financial guardrails and decision gates

Phase	Timing	Gate outcome
Initiate and baseline	Months 1–2	Confirm governance, owners, data, financial model and requirements
Foundation	Months 3–4	Accept architecture, control and integration readiness
Internal copilot	Months 5–7	Controlled pilot and productivity evidence
Customer assistant	Months 8–11	Controlled customer pilot, handoff and service evidence
Lending support	Months 12–15	Human-authorized pilot and rework evidence
Fraud assist	Months 16–18	Investigator pilot and false-positive evidence
Scale and transition	Months 19–24	Evidence-backed scale, operational acceptance and benefits handover

Financial control	Approved planning position	Authority boundary
CAPEX	\$11.5M	Planning ceiling, not a funding release
Annual OPEX	\$3.2M	Subject to staged/annual decisions
Five-year TCO	\$27.5M	Lifecycle envelope, not immediate spend
Initial release	\$0	Sponsor release after CFO validation

❏ Waterfall gates move the programme forward. Agile sprints deliver inside the line. A finished sprint is progress — not permission to scale.

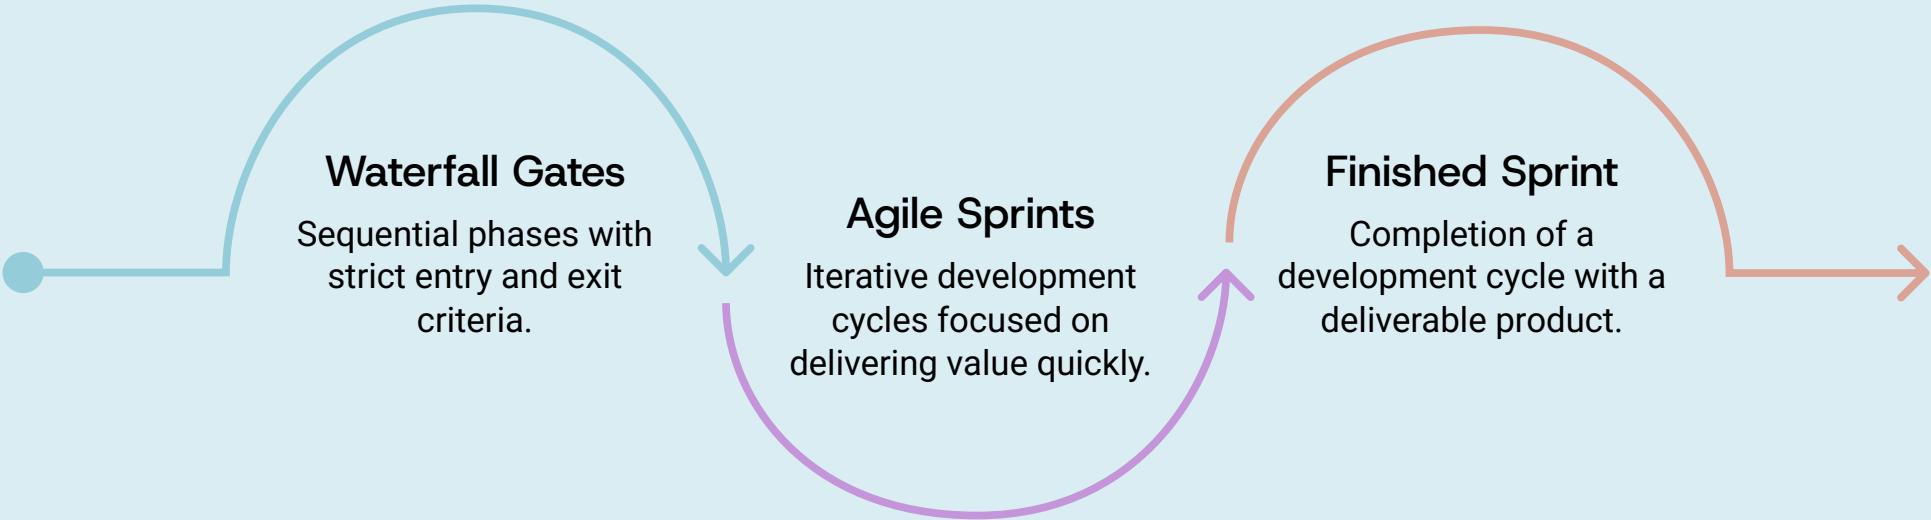

Stakeholder model: ownership, influence and engagement

Manage closely

Sponsor; Steering Committee; PM/AI PMO; CDO/COO/CIO; Security/Privacy; Risk/Model Risk; Compliance/Legal; CFO; Product Owners; Contact Centre; Lending; Fraud; Data Governance; core-system owners.

Keep satisfied


Internal Audit, Procurement/Vendor Management, Canadian regulatory obligations.

Keep informed and involved

Branch operations; agents and representatives; HR/L&D/Change; engineering/MLOps; employees; selected vendor; customers represented through research and accessibility evidence.

Accountability area	Accountable role	Core relationship
Programme baselines, material change and scale	Sponsor	Consolidated decision authority
Roadmap, evidence, RAID and escalation	PM / AI PMO	Integrates all four document baselines
Architecture and AI foundation	CIO / Enterprise Architecture	Enables safe, reusable delivery
MVP value and acceptance	Relevant Product Owner	Owns use-case outcomes and pilot evidence
Financial baselines and funding evidence	CFO	Validates investment case and releases
Control evidence	Security, Privacy, Risk, Compliance and Legal	Validates conditions before gate decisions

Engagement cadence: monthly register review; decision packs five working days before every gate; event-driven review after material change, incident, vendor appointment, funding decision or phase transition.

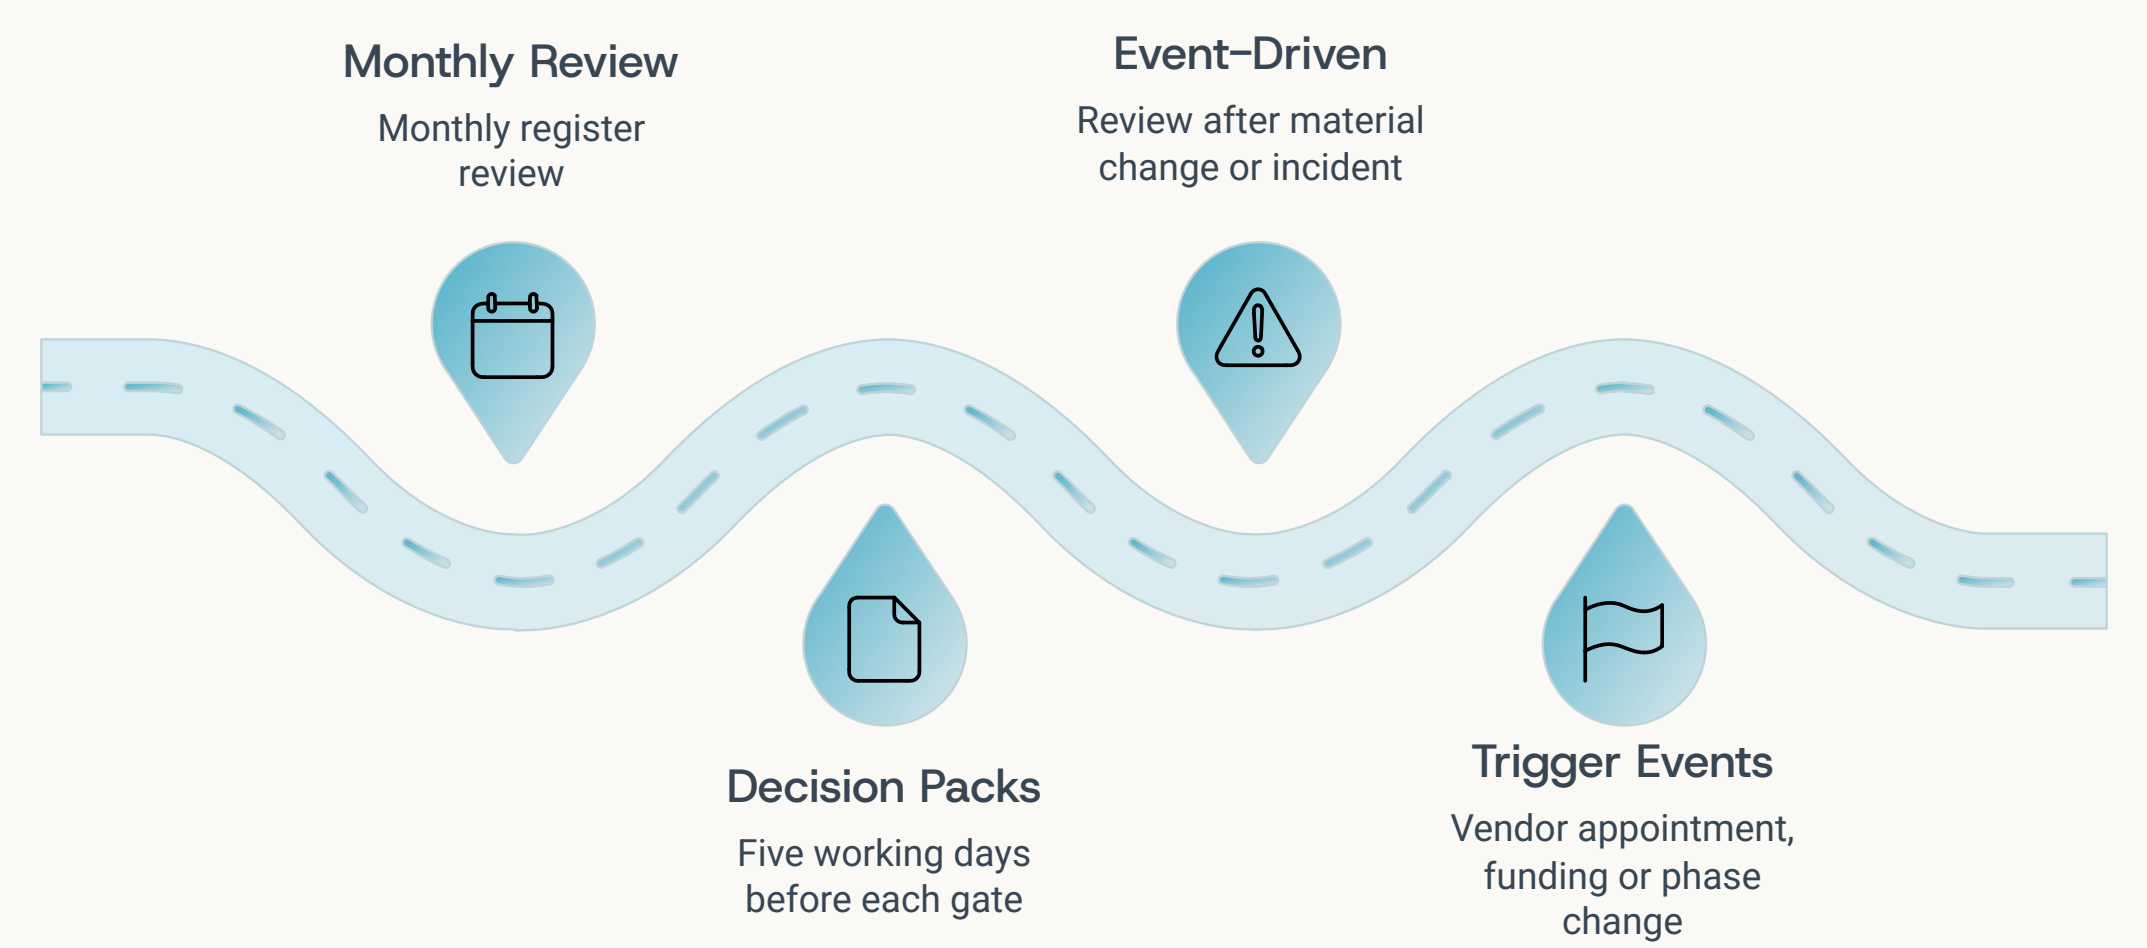


The Scope Plan translates the Charter into a traceable execution baseline.

Level	Controlled structure
Level 1	8 branches: Governance; AI foundation; Internal Copilot; Customer Assistant; Lending Support; Fraud Assist; Change/Benefits; Scale/Closure
Level 2	16 major deliverables: two integrated delivery components within each branch
Level 3	48 numbered work packages: lowest planning level for later responsibility, estimation, scheduling and monitoring

Representative work-package logic:

- Governance: confirm Sponsor authorization, record delegation limits, establish baselines, operate decision/change gates.
- Foundation: approve responsible-AI principles, complete architecture/integration/data-control work.
- MVPs: validate use cases, approve requirements, configure controlled capabilities, test and collect pilot evidence.
- Change/benefits: assess impacts, train roles, measure adoption and validate benefits.
- Scale/closure: consolidate evidence, prepare Sponsor decision, transition operations and complete post-implementation review.


 **Relational insight:** The WBS is not a task list in isolation. Every branch links to a Charter milestone, stakeholder evidence owner, acceptance criterion and Sponsor decision route.

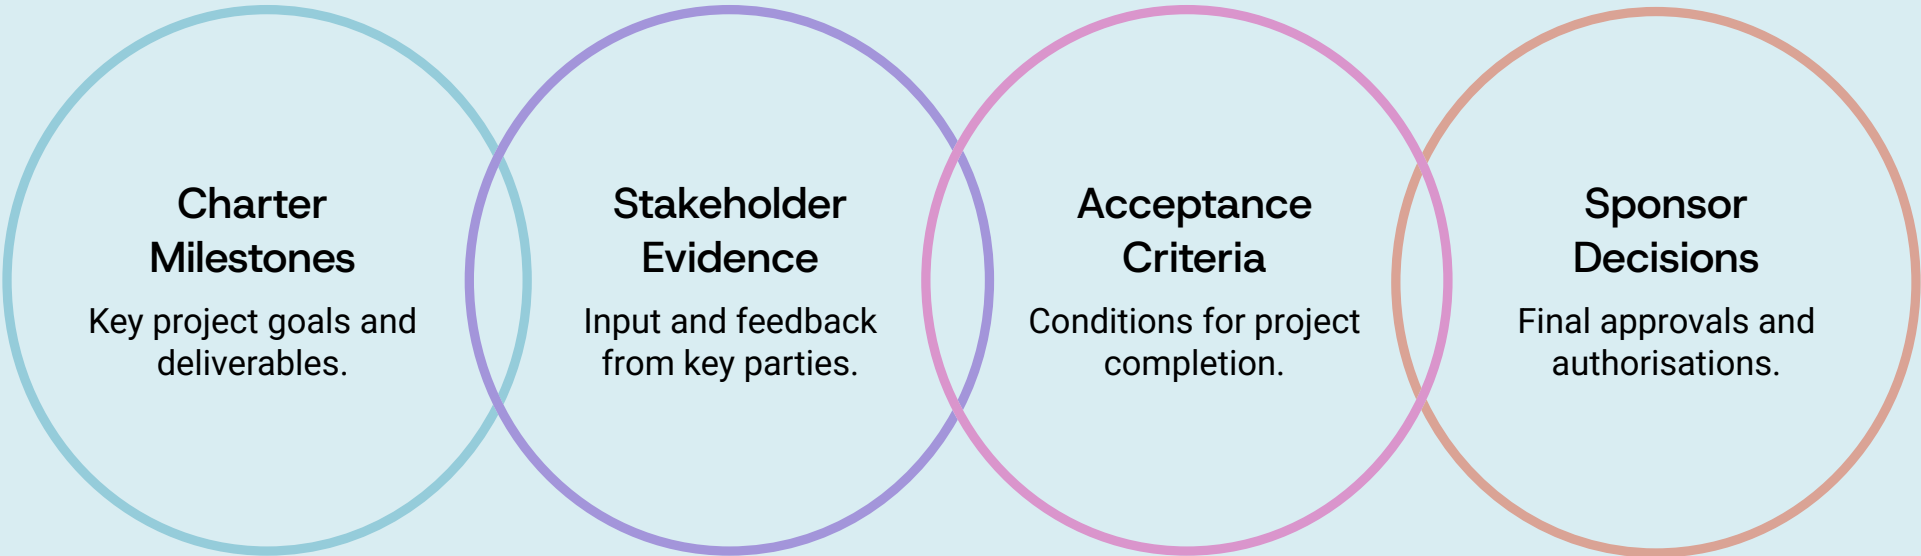

Value realisation: objectives, evidence and control measures

Approved target	Evidence required	Accountable evidence owner
35% fewer repetitive inquiries	Baseline, controlled pilot result, knowledge/handoff/audit evidence	Contact Centre / Digital Product Owner
30% lower report-preparation time	Comparable time study, governed use cases and human-verification guidance	COO / Copilot Product Owner
35% lower lending-documentation rework	Rework baseline/result, traceable summaries, human authority/override record	Lending Operations / Credit Risk
25% fewer fraud false positives	Labelled sample, parallel monitoring, investigator review, no automatic action	Fraud Operations / Financial Crime
>60% adoption	Defined active-use rule, dashboard, training and support readiness	Change Lead / Product Owner
Zero critical compliance breaches	Control checklist, incident and audit evidence	Risk, Compliance, Privacy and Security
Positive five-year NPV	Finance-approved cash-flow timing, baselines and attribution	CFO


 **Control principle:** Proposed operational guardrails (for example handoff accuracy, CSAT and audit completeness) cannot silently replace approved targets; they require evidence and a Sponsor decision under the controlled decision register.

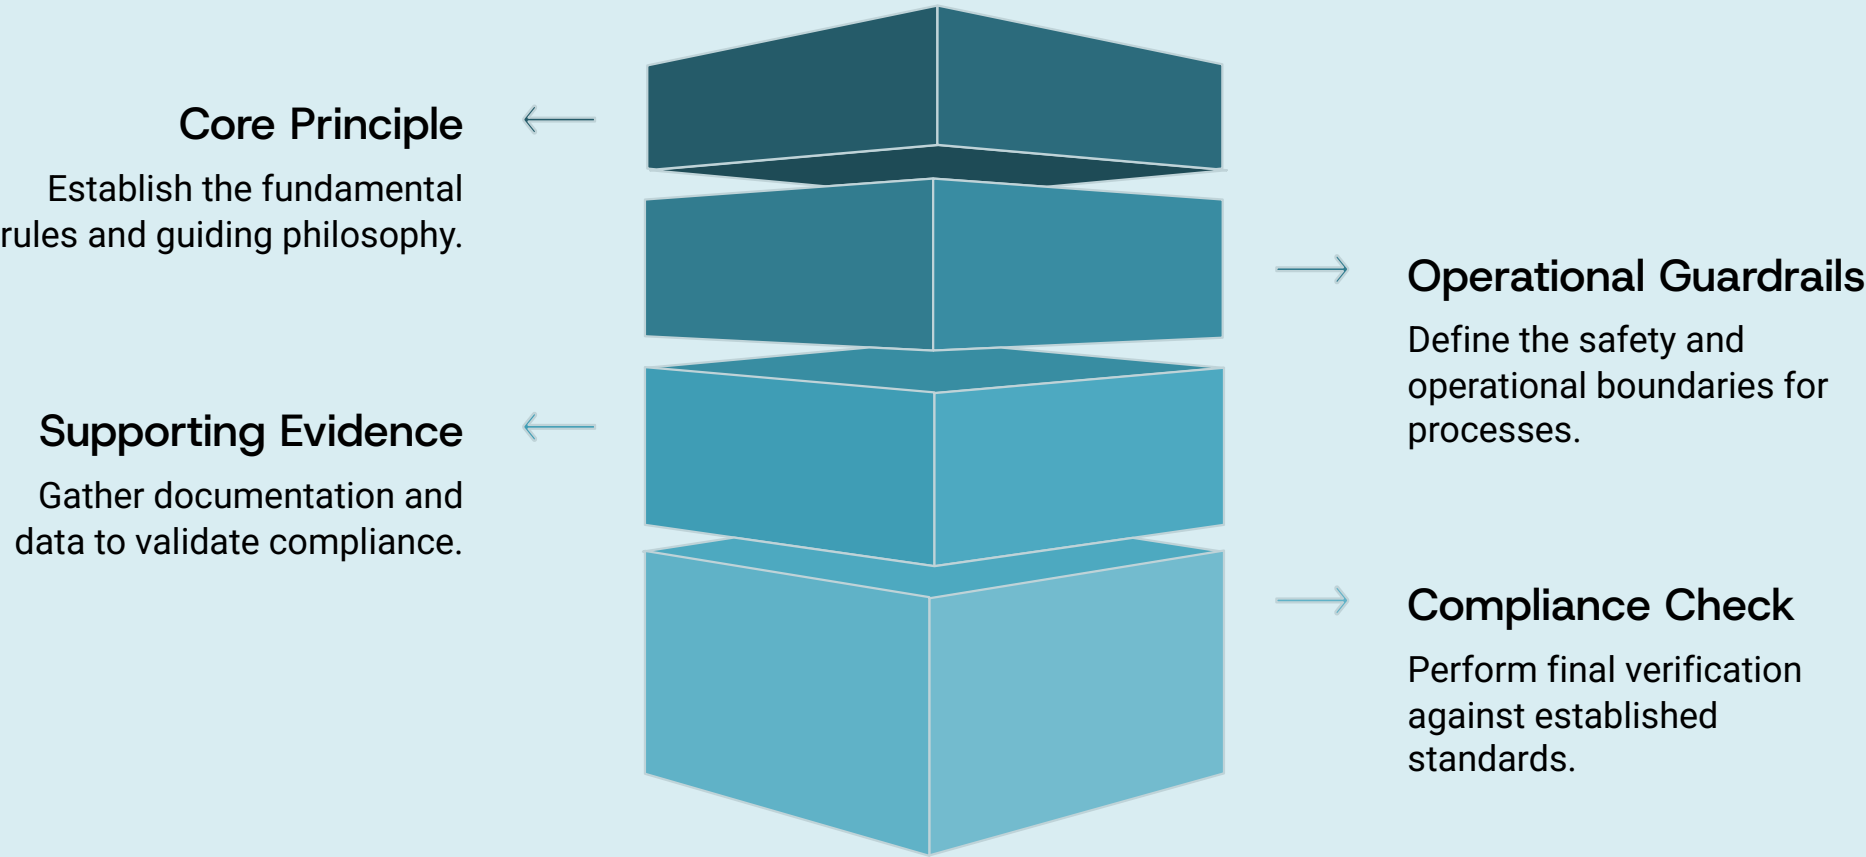

Risk, control and change-management model

Risk area	Required control response	Gate implication
Programme complexity / benefit dilution	Modular releases, dependency control, stage gates and benefit evidence	Do not scale without cross-pilot proof
Privacy, security and regulatory exposure	PIA, access control, masking, logging and applicable compliance evidence	Affected pilots cannot proceed without validation
Bias, error or AI overreliance	Explainability, fairness testing, confidence rules, human review and overrides	Human authority remains explicit
Data, integration or vendor uncertainty	Data-quality checks, architecture readiness, due diligence and service controls	No build/contract commitment before evidence
Adoption resistance	Co-design, training, champions, service support and feedback loops	Readiness evidence is part of acceptance

Scope and change workflow

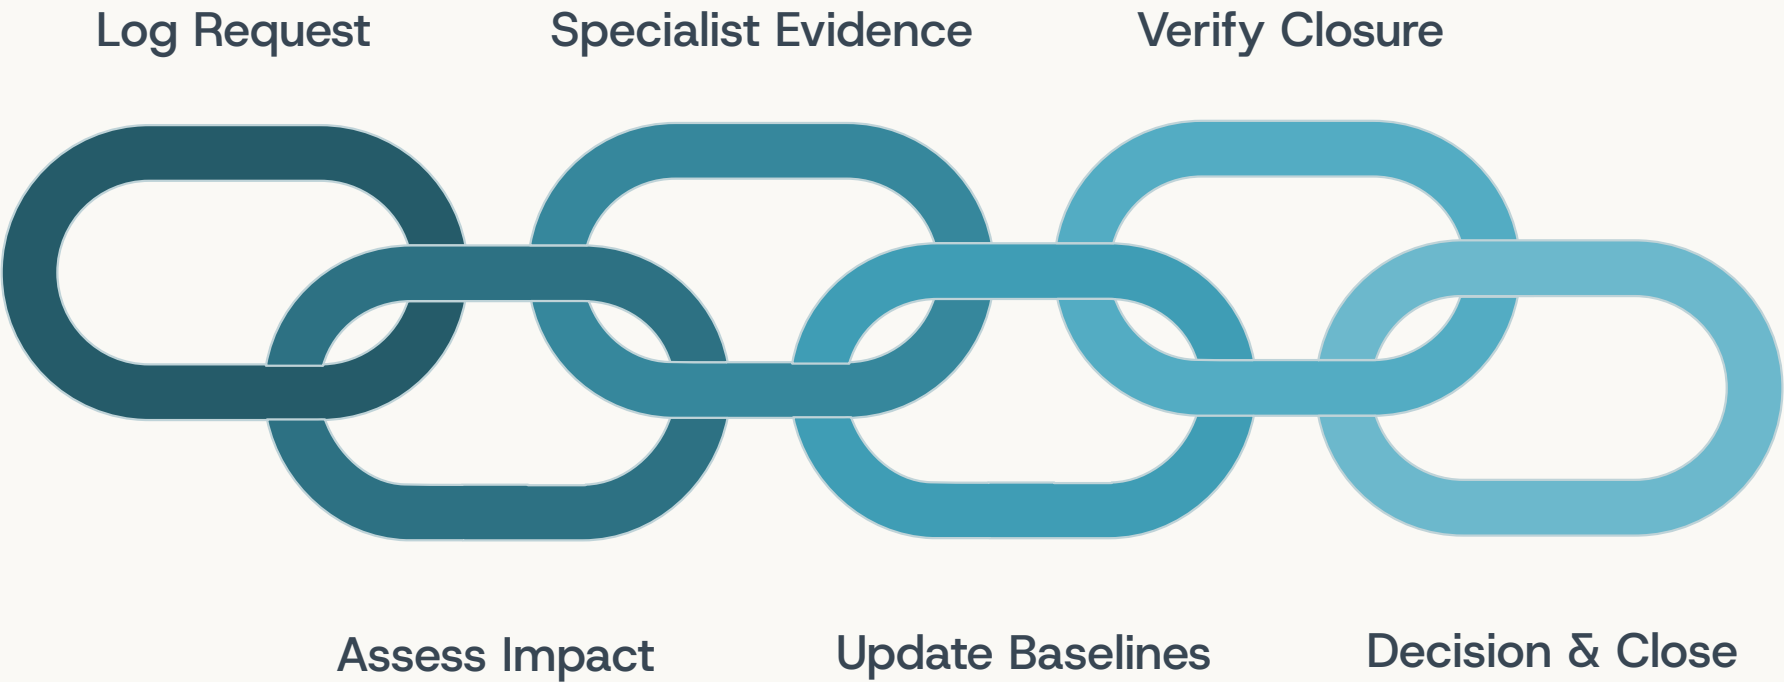

 **Boundary:** An Agile backlog item is not a scope authorization. Until formal delegation is recorded, material changes route to the Sponsor.

Executive actions: convert approval into controlled progress

- 1

Preserve the approved four-document pack

as the single source of truth for programme decisions.
- 2

Confirm formal decision rights

PM delegation boundaries, Steering Committee terms and accountable product/control owners.
- 3

Direct Finance

to validate cash-flow timing, benefit attribution and the first funding-gate proposal; initial commitment authority remains \$0 until released.
- 4

Complete readiness evidence

for architecture, data, security, privacy, model risk, compliance, legal and third-party controls before execution commitments.
- 5

Authorize progression only at evidence-backed gates

stop, remediate, continue, pilot, scale or close.

Closing message

Pole Trust Bank now has a sponsor-approved, stakeholder-aware and scope-controlled route to enterprise AI value. Success depends on keeping the four documents integrated: the business case defines the value, the Charter governs it, stakeholders supply ownership and evidence, and the Scope/WBS makes delivery traceable and controllable.

